

**South Shore Road Improvements Project
Bi-Weekly Progress Report
May 2, 2016 - May 13, 2016**

This report identifies the work on the Main Street project that N Granese Inc. has completed in the last two (2) weeks and is anticipated to be working on during the next two (2) weeks.

Last Two (2) Weeks

- Installed 3" Low Pressure Sewer Main on Lake Shore Road from Brookdale through the beginning of South Shore Road.
- Installed the related services for the homeowners within these limits.
- Installed 3 required Sewer Manholes within these limits as well.
- Liberty Utilities has been on-site setting new utility poles.




Sewer Service installed at green stake



Temporary Detour, and Traffic Maintenance, assisted with Town Officers



Lake Shore Road Sewer Main Installation

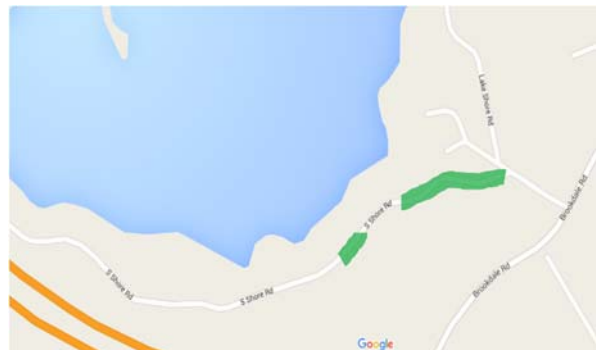

Green indicates anticipated work from May 2, 2016 through May 13, 2016.

Next Two (2) Weeks

- Begin sewer work on South Shore Road, with required Main, Services, and Manholes.
- Liberty Utilities will be on-site conducting tree removal operations for new utility pole locations
