

South Broadway Sewer, Water, and Bridge Improvements

Bi-Weekly Progress Report

February 20, 2020

This report identifies the work on the South Broadway Sewer, Water, and Bridge Improvements Project that DeFelice Corp. has completed in the last 2 weeks and anticipates to be working on during the next two (2) weeks. Roads will remain open during the day, expect delays. There may be some night time work with alternating traffic around the work zone. Officers will help you pass through the work zones. Thank you for your patience during the construction.

Last Two (2) Weeks


- Phase 2 Bridge Footings were installed, cured, and backfilled
- Stream bed was installed
- Bridge sidewalls and top deck were installed
- Bridge wingwalls were installed



Bridge Section Installation



Bridge Section Installation

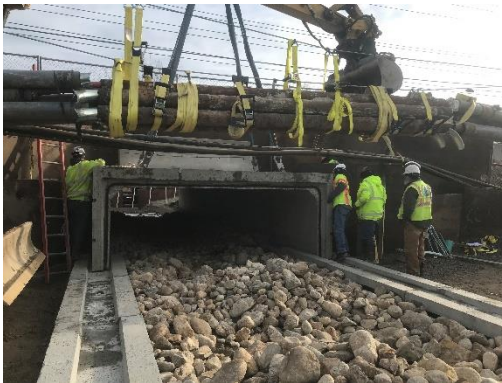

Bridge Section Installation with suspended utilie



Bridge Deck with Wingwalls Installed

Next Two (2) Weeks

- Phase 2 Bridge construction to continue on South Broadway near Westchester Street.
 - Continue utility coordination
 - Waterproof membrane installation on Bridge
 - Grading around Bridge
 - Prep for pavement operations

Construction Hotline: 978-726-2873
(for general inquiries, questions and complaints)
