


**South Policy Street Reconstruction Project
Bi-Weekly Progress Report
September 3, 2014**

This report identifies the work on the South Policy Street project that G.E. Merrill & Sons Excavating Inc. has completed in the last two (2) weeks and is anticipated to be working on during the next two (2) weeks.

Last Two (2) Weeks

- Completed Remove/Rehandle of the Reclaim South of Route 38
- Completed Base and Binder Course Paving South of Route 38
- Continued Granite Curb and Cape Cod Berm Installation
- Completed Base Course Paving of Driveways South of Route 38
- Continued Loam and Seed Operations

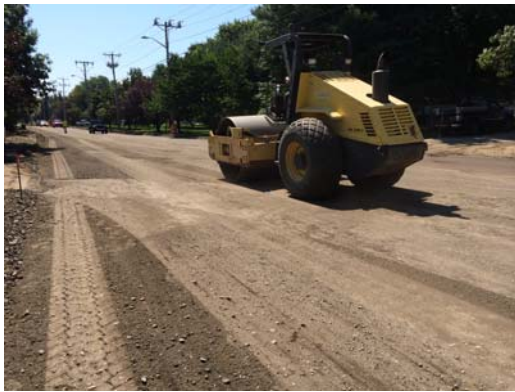

8/25/2014 – Fine Grading South of Route 38



8/26/2014 – Base Course Paving South of Route 38

Next Two (2) Weeks

- Complete Granite Curb and Cape Cod Berm Installation
- Complete Base Course Paving of Driveways South of Route 38
- Complete Sidewalk Construction
- Perform Milling of the Route 38/South Policy Street Intersection.
- Complete Loam and Seed Operations
- Complete Top Course Paving Operations
